Little Eaton Village Hall

10/09/2009 | Little Eaton Parish Council | DC

Line	Name
	Enabling Works
1	Erect Temp fencing & set up site accommodation
2	Remove stone wall & form access road
3	Reduce level excavation
4	***Temporary carpark access restrictions***
	Sup structure Works
5	Retaining wall Construction
6	Tanking & Waterproofing
7	Backfill to RW
	Superstructures
8	Masonry upto first floor level
9	PCU plank & stairs
10	Masonry upto wall plate level
11	Roof Carcassing
12	Construct gables
13	Install soffit & Fascias
14	Roof coverings
15	Install External window & doors
	Internal Fit Out
16	First Fix mech & electrical (incl underfloor heating)
17	Floor screeds
18	Plastering
19	Second fix
20	Ceramic Tiling
21	Decorations
22	Floor Finishes
23	Third Fix / kitchen installation
24	Snag / cleanout & handover
25	Contract completion

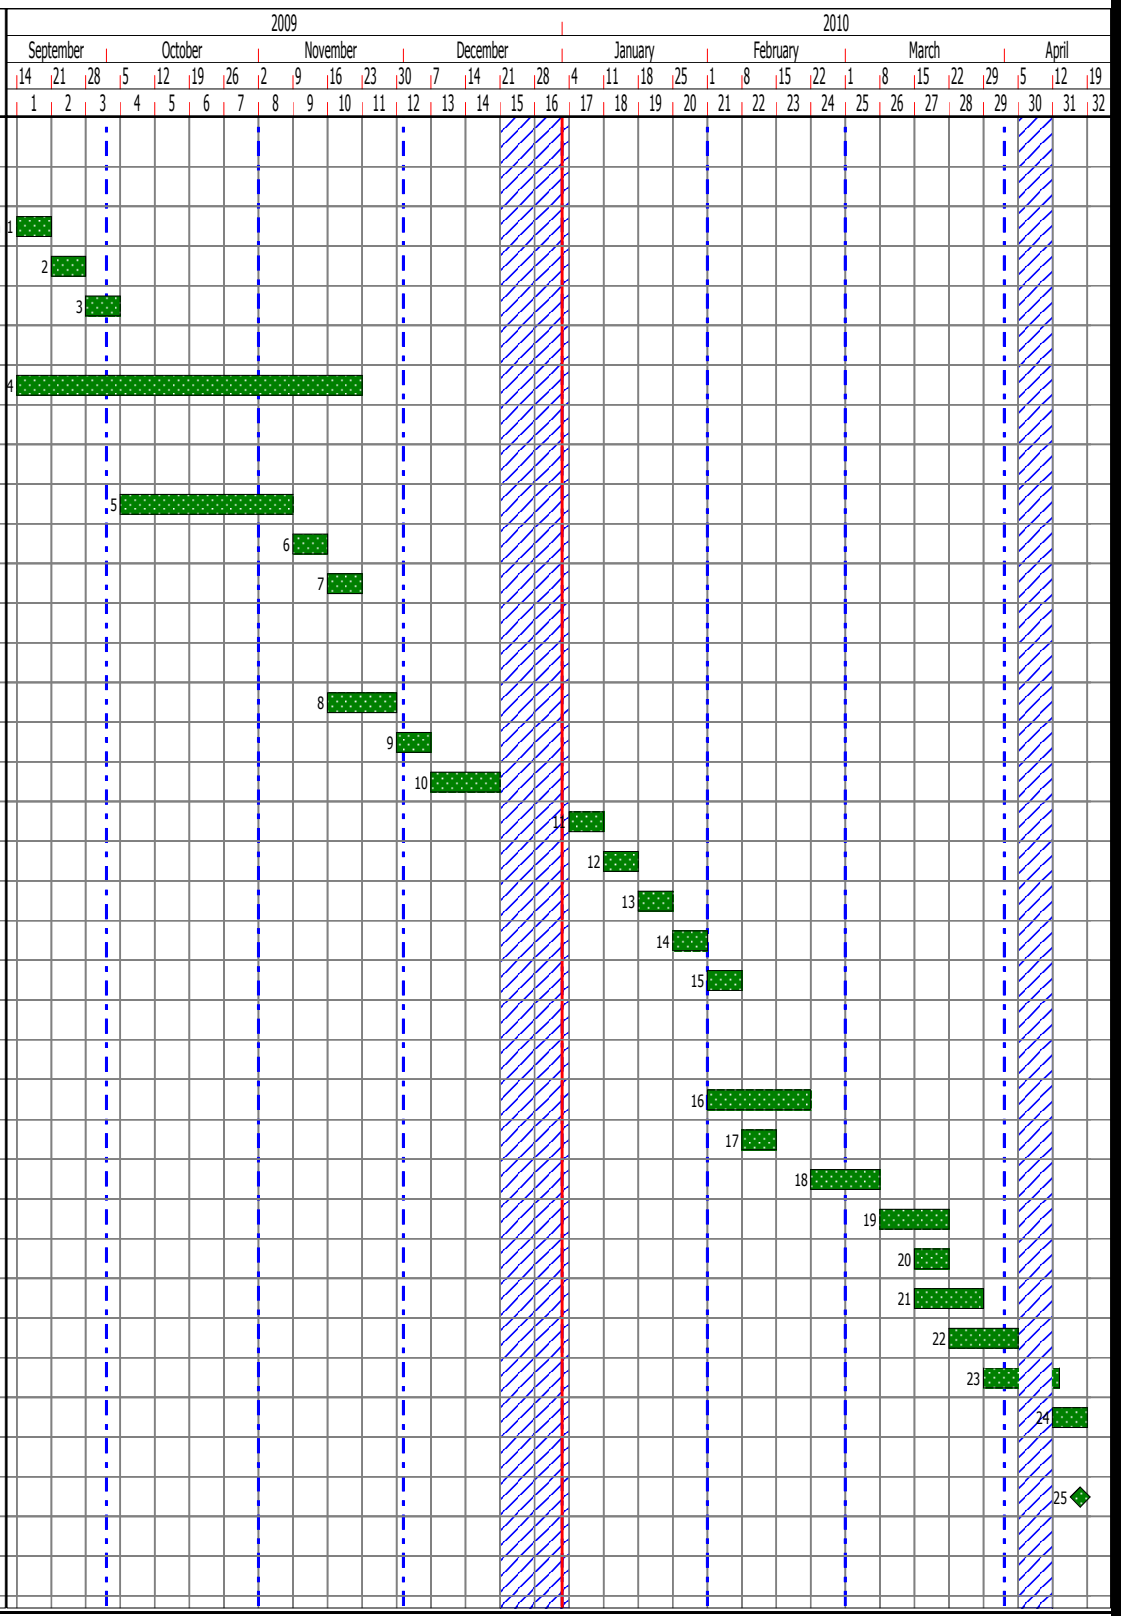

Page 1 of 1

Drawn by: Planner - Chart Properties	Dwg No. 00001	Revision No. A	Notes: Comment - Chart Properties

Project Ref. R:\E Projects\E214 Extension of Little Eaton Village Hall\F Programmes\Little Eaton Village Hall - Contract Programme.pp

Planned By Asta Powerproject
